ID	Task Mode	Task Name	Duration	Start	Finish
1		Bidding	5 days	Fri 4/30/21	Thu 5/6/21
2		Owner Award	14 days	Fri 5/7/21	Wed 5/26/21
3		Critical & Initial Awards	10 days	Thu 5/27/21	Wed 6/9/21
4		Steel Leadtime	190 days	Thu 6/10/21	Wed 3/2/22
5		Summer 21 Float	25 days	Thu 6/10/21	Wed 7/14/21
6		Field Start	1 day	Thu 7/15/21	Thu 7/15/21
7		Clearing, Earthwork, Pad	20 days	Thu 7/15/21	Wed 8/11/21
8		Foundations	31 days	Thu 8/12/21	Thu 9/23/21
9		Load Bearing CMU	23 days	Fri 9/24/21	Tue 10/26/21
10		Winter 21-22 Float	90 days	Wed 10/27/2	Tue 3/1/22
11		Steel & HC Erection	20 days	Thu 3/3/22	Wed 3/30/22
12		UG MEP, SOG, Toppings	20 days	Thu 3/31/22	Wed 4/27/22
13		Exterior Studs & Sheating	25 days	Thu 4/28/22	Wed 6/1/22
14		Exterior Veneer & Siding	30 days	Thu 6/2/22	Wed 7/13/22
15		Exterior Glass	20 days	Thu 7/14/22	Wed 8/10/22
16		Flat Roof	15 days	Thu 5/12/22	Wed 6/1/22
17		Metal Roof	20 days	Thu 6/2/22	Wed 6/29/22
18		OH MEP Rough	20 days	Thu 6/2/22	Wed 6/29/22
19		Interior Framing	15 days	Thu 6/30/22	Wed 7/20/22
20		In-Wall Rough	15 days	Thu 7/21/22	Wed 8/10/22
21		Board and Initial Paint	15 days	Thu 8/11/22	Wed 8/31/22
22		Interiors (all trades)	50 days	Thu 9/1/22	Wed 11/9/22
23		Site Paving, Landscape, Etc	40 days	Thu 7/14/22	Wed 9/7/22
24		Punchout, Inspections	10 days	Thu 11/10/22	Wed 11/23/2

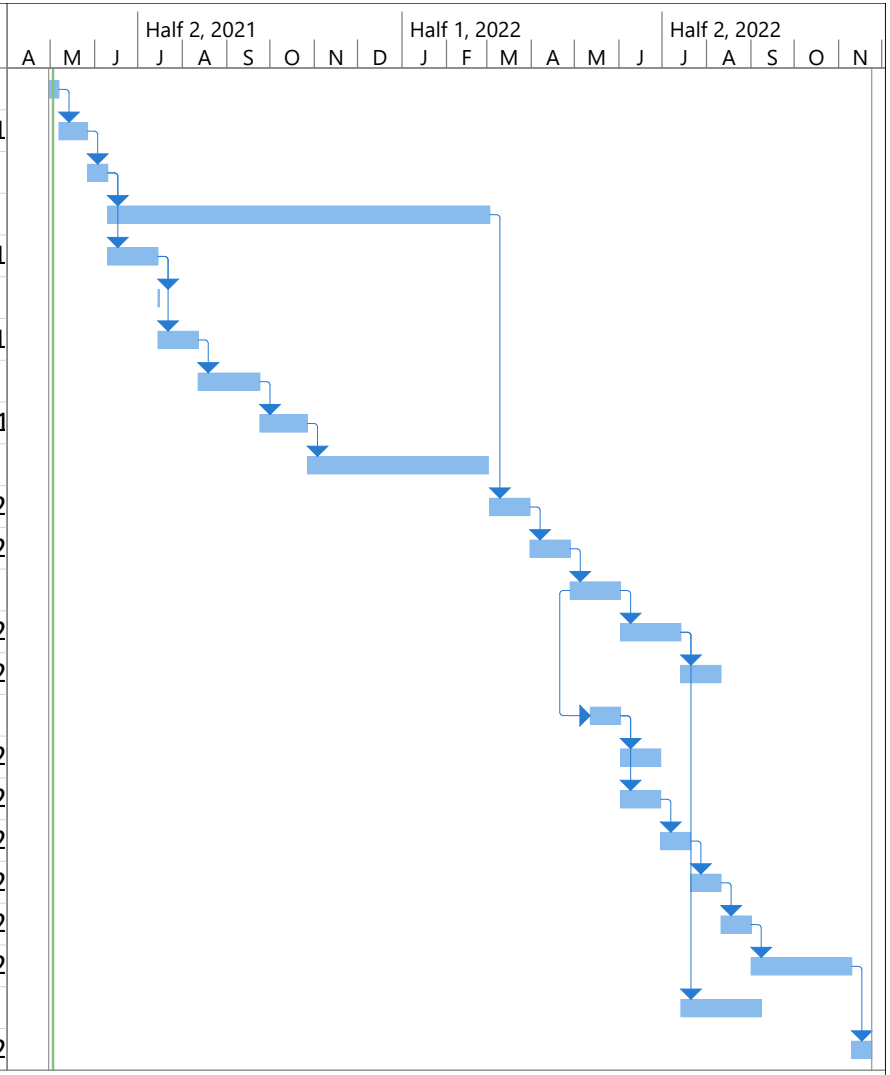

Project: Redford NFS - Prelim S
Date: Mon 5/3/21

Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress
